


City of Commerce City 2K Bond Program Monthly Executive Summary – February 2018

2K Revenue and Expenses

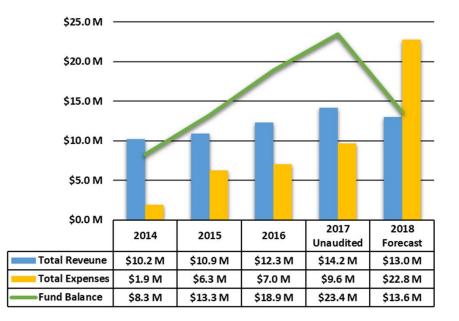

Bond Proceeds

Total Bond Limit:	\$166,000,000
First Bond Issuance - 2014:	\$78,000,000
Second Bond Issuance - 2016:	\$66,000,000
Interest thru 2016:	\$76,417
Total Bond Funding:	\$144,076,417
Other Funding:	\$3,370,253
Expenditures to Date:	\$111,836,652

2018 Gross Tax Revenue



Project Budgets, Commitments and Expenditures

Projects	2K Bond Funding	Other Funding	Total Budget	Committed	% Committed	Expended	% Expended
•Program Level Budgets	4,341,599		4,341,599		0.00%		0.00%
Bison Ridge Recreation Center							
Recreation Center	44,823,873	5,667	44,829,540	40,810,455	91.03%	37,357,107	83.33%
•Site & Roadway Infrastructure	19,571,737	1,267,947	20,839,684	19,486,958	93.51%	19,486,958	93.51%
•Eagle Pointe Recreation Center Renovation	16,911,069	469,000	17,380,069	14,211,123	81.77%	1,190,992	6.85%
•Paradice Island Pool at Pioneer Park	8,649,326	518,281	9,167,607	9,151,107	99.82%	9,151,107	99.82%
•3 New Neighborhood Parks							
•Fronterra Neighborhood Park	3,389,060	224,957	3,614,017	3,614,017	100.00%	3,578,527	99.02%
•Turnberry Neighborhood Park	2,258,521	219,179	2,477,700	2,477,700	100.00%	2,477,700	100.00%
•Villages East Neighborhood Park	2,160,730	165,222	2,325,952	2,325,952	100.00%	2,325,952	100.00%
•Tower Road Widening	41,970,502	500,000	42,470,502	40,410,445	95.15%	36,268,308	85.40%
Total	144,076,417	3,370,253	147,446,670	132,487,756	89.85%	111,836,652	75.85%

Project Phase Highlights

out	Paradice Island Pool at Pioneer Park ✓ Complete
	3 New Neighborhood Parks
	Fronterra Park
	✓ Complete
	Turnberry Park
	✓ Complete
	Villages East Park
	✓ Complete
	Tower Road Widening
	Roadway substantially complete

• T-88 drainage work continues

Project Status

Phase 1	Phase 2	Phase 3	Phase 4	Phase 5	Phase 6	Phase 7
Planning	Pre-Design & RFP	Design	Const. Bid & Award	Construction	Acceptance	Closeout
					X	
					\mathbf{x}	
					X	
					-77-	
					X	
				\mathbf{x}		
		Pre-Design &	Pre-Design &	Pre-Design & Const. Bid &	Pre-Design & Const. Bid &	Pre-Design & Const. Bid &



Bison Ridge Recreation Center & Infrastructure

- Infrastructure substantially complete
- Continued interior construction and exterior enclosure
- Continued FF&E Procurement
- Grand Opening event planned May 25th

Eagle Pointe Recreation Center Renovation

- Awarded Final GMP Contract
- Continued foundations for new addition
- Started demolition of south entry



City of Commerce City 2K Bond Program Report Description



Report Number 0101 - Monthly Executive Summary

Issued on the third Monday of the month with status through the end of the previous month (unless otherwise stated)

2K Revenue and Expenses

- Revenue includes the 1% sales and use tax as well as revenue from 2K facilities such as Paradice Island Pool and the new Bison Ridge Recreation Center
- Expenses include bond debt payments, program management, operation and maintenance of 2K facilities and transfers to CIPP projects
- The numbers represented are 2014, 2015, 2016 and 2017 (unaudited) actuals. Numbers for 2018 are forecasts.

Year to Date Gross Revenue

• Revenue reporting can lag between 2 to 3 months. The status date for revenue is as noted.

Bond Proceeds

- Total Bond Limit total amount of debt authorized through the 2K bond measure
- Current 2K Budget budget established to deliver the first five 2K projects
- First Bond Issuance first sale of bonds in 2014 to fund the program
- Second Bond Issuance second sale of bonds in 2016 to fund the program
- Interest thru 2016 interest earned on investment of bond proceeds through 2016.
- Total Bond Funding total funding available from 2014 and 2016 bond sales and interest earnings
- Other Funding Other funding sources applied to 2K projects, this has primarily been in the form of grants
- Expenditure to date Project expenditures against the bond funding. Expenditures are as current as possible through the reporting period, however some expenditures may lag due to invoice cycles

Project Status

• Matrix of projects and phases for the Capital Infrastructure Projects Program. Gives a quick indicator of what phase a project is in by the color of the box. Gray is a completed phase, blue is a phase in progress, green is a phase started in the current reporting period. Yellow stars indicate a project is open and available for public use

Budgets, Commitments and Expenditures

- 2K Budget Program and Project budgets were re-baselined as of September 2017 to reflect final costs for completed projects and other approved budget changes, project budgets may continue to be updated through the formal change management process
- Other Funds Amount of any other funding associated with a project such as grants or reimbursements from other organizations for work done on their behalf in association with a project
- Total Budget Total of 2K budget plus any other funding for the project
- Committed The sum of outstanding contracts, purchase orders and actual costs incurred on the project
- % Committed Committed dollar amount divided by total budget
- Expended Actual costs incurred on the project
- % Expended Expended dollar amount divided by total budget

Project Phase Highlights

• A brief list of recently completed activities and upcoming events for each active project
