




City of Commerce City

2K Bond Program

Monthly Executive Summary – May 2017


2K Revenue and Expenses

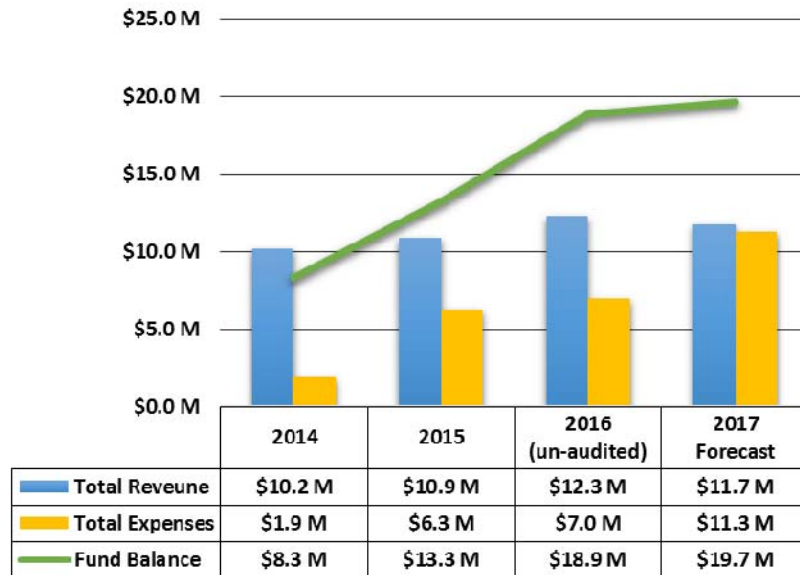

Bond Proceeds

Total Bond Limit: \$166,000,000
First Bond Issuance - 2014: \$78,000,000
Second Bond Issuance - 2016: \$66,000,000
Total Bond Funding: \$144,000,000
Other Funding: \$2,285,958
Expenditures to Date: \$60,921,201

2017 Gross Revenue



Project Budgets, Commitments and Expenditures

Projects	2K Budget	Other Funds	Total Budget	Committed	% Commit	Expended	% Exp
•Program Level Budgets	6,387,470		6,387,469		0.00%		0.00%
•New Recreation Center							
•New Recreation Center	45,327,651		45,327,651	39,005,219	86.05%	13,184,822	29.09%
•Site & Roadway Infrastructure	19,947,983	1,267,677	21,215,660	18,905,876	89.11%	9,892,154	46.63%
*Existing Recreation Center Expansion	10,000,000		10,000,000	1,113,785	11.14%	280,802	2.81%
*Outdoor Pool at Pioneer Park	8,804,799	518,281	9,323,080	9,323,080	100.00%	9,151,107	98.16%
*3 New Neighborhood Parks							
*Fronterra Neighborhood Park	3,414,016	200,000	3,614,016	3,614,016	100.00%	3,578,527	99.02%
*Turnberry Neighborhood Park	2,326,949	150,000	2,476,949	2,476,949	100.00%	2,466,273	99.57%
*Villages East Neighborhood Park	2,287,043	150,000	2,437,043	2,374,091	97.42%	2,314,525	94.97%
•Tower Road Widening	45,504,089		45,504,089	35,643,032	78.33%	20,052,991	44.07%
Total	144,000,000	2,285,958	146,285,957	112,456,047	76.87%	60,921,201	41.65%

Project Status

Project Name	Phase 1	Phase 2	Phase 3	Phase 4	Phase 5	Phase 6	Phase 7
	Planning	Pre-Design & RFP	Design	Const. Bid & Award	Construction	Acceptance	Closeout
New Rec Center Site & Roadway Infrastructure							
New Recreation Center							
Existing Recreation Center Expansion							
Outdoor Pool at Pioneer Park						★	
Fronterra Neighborhood Park						★	
Turnberry Neighborhood Park						★	
Villages at Buffalo Run East Neighborhood Park						★	
Tower Road Widening							

Phase completed
 Phase in progress
 Phase started this month
 ★ Open for community use

Project Phase Highlights

Outdoor Pool at Pioneer Park

✓ Complete

3 New Neighborhood Parks

Fronterra Park

✓ Complete

Turnberry Park

✓ Complete

Villages at Buffalo Run East Park

✓ Complete

Existing Recreation Center Expansion

• Completed Schematic Design

New Recreation Center & Infrastructure

- Infrastructure Roadway and Utility work continues
- Continued structural steel erection and started gym roofing
- Continued parking lot curb and gutter

Tower Road Widening

- Segment 1 – Traffic switched over to new box culvert on May 30th
- Segment 2 – Street lighting installed
- Segment 3 – Continuing subgrade, utility and drainage work



City of Commerce City

2K Bond Program

Report Description



Report Number 0101 - Monthly Executive Summary

Issued on the third Monday of the month with status through the end of the previous month (unless otherwise stated)

2K Revenue and Expenses

- Revenue includes the 1% sales and use tax as well as revenue from 2K facilities such as Paradise Island Pool
- Expenses include bond debt payments, program management and operation and maintenance of 2K facilities
- The numbers represented are 2014 & 2015 actuals, 2016 un-audited actuals. Numbers for 2017 are forecasted.

Year to Date Gross Revenue

- Revenue reporting can lag between 2 to 3 months. The status date for revenue is as noted.

Bond Proceeds

- Total Bond Limit – total amount of debt authorized through the 2K bond measure
- Current 2K Budget – budget established to deliver the first five 2K projects
- First Bond Issuance – first sale of bonds in 2014 to fund the program
- Second Bond Issuance – second sale of bonds in 2016 to fund the program
- Total Bond Funding – total funding available from 2014 and 2016 bond sales
- Other Funding – Other funding sources applied to 2K projects, this has primarily been in the form of grants
- Expenditure to date – Project expenditures against the bond funding. Expenditures are as current as possible through the reporting period, however some expenditures may lag due to invoice cycles

Project Status

- Matrix of projects and phases for the Capital Infrastructure Projects Program. Gives a quick indicator of what phase a project is in by the color of the box. Gray is a completed phase, blue is a phase in progress, green is a phase started in the current reporting period. Yellow stars indicate a project is open and available for public use

Budgets, Commitments and Expenditures

- 2K Budget - Program and Project budgets were re-baselined as of December 2016 to reflect final costs for completed projects and other approved budget changes, project budgets may continue to be updated through the formal change management process
- Other Funds – Amount of any other funding associated with a project such as grants
- Total Budget – Total of 2K budget plus any other funding for the project
- Committed – The sum of outstanding contracts, purchase orders and actual costs incurred on the project
- % Committed - Committed dollar amount divided by total budget
- Expended - Actual costs incurred on the project
- % Expended - Expended dollar amount divided by total budget

Project Phase Highlights

- A brief list of recently completed activities and upcoming events for each active project
